



CONSTRUCTION MONITORING REPORT

Eversource Transmission Lines:
F107

**Madbury, Durham,
Newington, Portsmouth, NH**

Alteration of Terrain Permit:
SEC Docket No. 2015-004

Environmental Permit:
SEC Docket No. 2015-004

USEPA NOI Tracking No:
**NHR1000QN
NHR1000QT
NHR1000QO
NHR1000S6**

NAI Project No:
23840.39

TYPE OF INSPECTION: Weekly Storm Event Incident Corrective Action

Date: **01/23/20** Time: **8:00am** Does this report include a 0.25" storm event? Yes No
If yes, how did you determine whether a 0.25" storm event has occurred? Rain Gauge Weather Station
Storm event information is from Pease Air Force Base.

+Storm event information (approx.):	Start date:	Amount (inches):
	Start date:	Amount (inches):
	Start date:	Amount (inches):

NOTE:
* 01-18-20: site received 6.00in of snow.

Inspector name(s), title(s) and qualifications: **Matthew Smith, Normandeau Environmental Inspector and Marc Jacobs, CPESC, NHCWS**

Others present/qualifications(s): **Sam Eames, Eversource construction representative**

Weather conditions (since last inspection): **Clear, with temperatures in the 20's and 30's.**

Weather conditions (time of inspection & future outlook): **Clear, temperature in the 20's. Future forecast shows rain showers over the weekend with temperatures in the 30's.**

CONSTRUCTION SITE SEQUENCING AND DISTURBANCE
Disturbed area and ongoing work (acreage & description): < 1 acre

Proceeding per approved plan? Yes No, if not, note area and explain:

Operating within phasing limitations? Yes No, if not, note area and explain:

General Comments

- Continued BMP maintenance and upkeep is a constant priority on shorelines of both sides of the Bay during the winter months.
- Housekeeping such as sweeping of timber mats and roads is a must.
- All required BMPs need to be installed before construction activities.
- All contractors on site should have a copy of the construction drawings.
- During mat removal be sure to remove any remains of silt socks etc.

Work completed this week:

- *Portsmouth*
 - *Boulos continues to do work at substation.*
- *Newington*
 - *GZA continues to manage soils excavated during construction activities.*
 - *JCR installed Strs. 119-121.*
- *Durham.*
 - *JCR continues to build access roads from Strs. 61-72.*
 - *JCR is excavating foundation for Str.70.*
 - *JCR set cans for Strs. 71-72.*
 - *JCR is removing mats at Str's. 1-3.*
 - *MJ continues to drill foundation for Str. 58.*

Erosion and sediment control items and observations:

- **BMPs**
 - All required BMPs need to be installed as access roads are being built, before construction starts.

Corrective Action

- None

OPERATING WITHIN LIMITS?

N/A YES NO if not, please explain:

SURFACE WATER QUALITY

Storm water discharge from the site at the time of inspection? YES NO N/A
Storm water discharge consistent with water quality standards? YES NO N/A
Turbidity visually observed? YES NO

If yes, check appropriate location(s) below, and describe discharge:

Location: N/A
Pond location: N/A
Adjacent surface water or wetland: N/A

Description: N/A.

TEMPORARY EROSION AND SEDIMENT CONTROLS (TESC)

Installed and functioning per the SWPPP? YES NO N/A

Are any corrective actions required? YES NO if so, please describe?

** Note: The permit differentiates between conditions requiring repairs and maintenance, and those requiring corrective action. Corrective actions are triggered only for specific, more serious conditions and require a corrective action form be filled out. Please refer to Part 5 of the CGP for additional information*

PERMANENT EROSION AND SEDIMENTATION CONTROLS

Disturbed areas must have a uniform perennial vegetative cover with 85% density, or equivalent physical stabilization, to be considered permanently stabilized (per the SWPPP).

Installed and functioning per the SWPPP? YES NO N/A

If not, explain what was not performed correctly (construction/stabilization) for each of the following categories. Detail what/where needs to be corrected, and what has been corrected since the last monitoring inspection.

If so, what areas: N/A

Areas that have been restored and mulched, but have little germination: Both sides of Little Bay. Trench between Strs. 106-107 (Frink farm-Hannah Lane). Strs. 28 & 29.

Moderate germination: Strs. 135 – 139.

Stabilized (85%+ germination): Field house at UNH, Colovos Rd at UNH, and College Brook at UNH.

OTHER COMMENTS AND OBSERVATIONS:

-None other than the above comments.

CERTIFICATION:

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."

This form is completed and signed in accordance with the Signatory Requirements specified in Appendix I.11 of the NPDES CGP for the project site and NOI identified above.

Authorized signature: _____

MARGIE JACOBS
CERTIFIED PROFESSIONAL
EROSION & SEDIMENT
CONTROL SPECIALIST
NO. 2017 EXP.

Date: _____ 01/23/20

PHOTOGRAPHS



Fig 1: Str. 112. Viewing northeast. (01-16-20).



Fig 2: Str. 111. Viewing south. (01-16-20).



Fig 3: Excavating foundation for Str. 72. Viewing northeast. (01-16-20).



Fig 4: Access road entrance to Gundalow landing/east side of the Bay. (01-17-20).

PHOTOGRAPHS



Fig 5: Str. 102. Viewing southwest in wetland NW6. (01-17-20).
Straw bales have since been staked in.

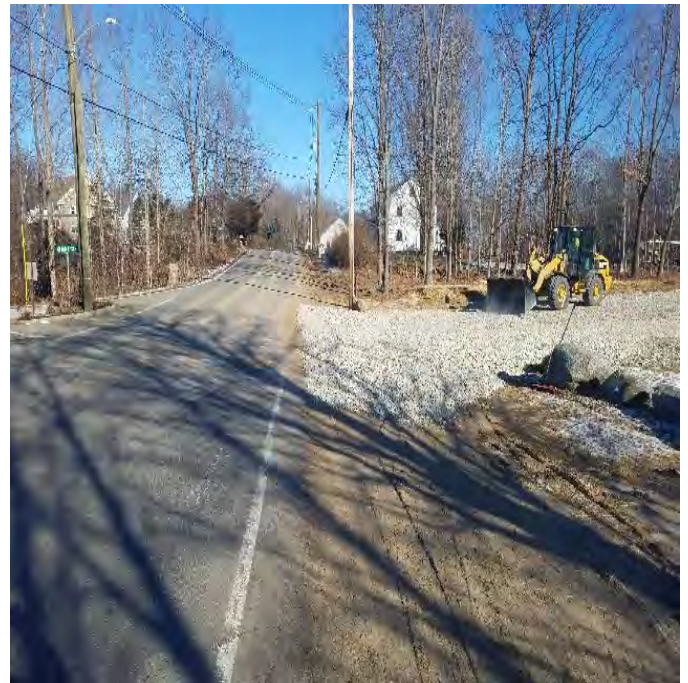


Fig 6: Stone added to access road entrance to Str. 107, off of Nimble Hill Road. Viewing north. (01-17-20).



Fig 7: Str. 110. Viewing northeast. (01-17-20).



Fig 8: Str. 111. Viewing northeast. (01-17-20).

PHOTOGRAPHS



Fig 9: Str. 109. In wetland NW26. Viewing northeast. (01-17-20).



Fig 10: Spreading straw over exposed soil around Str. 71 foundation cans. Viewing west. (01-20-20).



Fig 11: Timber bridge over stonewall WP-21. Viewing west. (01-20-20).



Fig 12: MJ drilling foundation for Str. 58. Viewing west. (01-21-20).

PHOTOGRAPHS



Fig 13: Crew installing Str. 119. Viewing northwest. (01-21-20).



Fig 14: Str. 120. Viewing north. (01-21-20).



Fig 15: Str. 2. Viewing south. (01-21-20).



Fig 16: Removing timber mats around Str. 3. Viewing south. (01-21-20).

PHOTOGRAPHS



Fig 17: Excavating foundation for Str. 70. Viewing west. (01-21-20).



Fig 18: Access road through wetland DW9. Viewing west. (01-22-20).



Fig 19: Dewatering basin at Str. 70. Viewing east. (01-22-20).



Fig 20: Excavating foundation for Str. 70. Viewing east. (01-22-20).

PROJECT TEAM

Eversource

Attn: Dena Champy-Eversource Project
Manager

Phone: 603-634-2891

Email: dena.champy@eversource.com

Attn: Tom Sullivan-Construction
Management

Phone: 078-502-3805

Email: thomas.sullivan@eversource.com

Attn: Joseph Sperry-Eversource Senior
Engineer

Phone: 603-634-2562

Email: joseph.sperry@eversource.com

Attn: Kurt Nelson-Eversource Permitting

Phone: 603-714-3031

Email: kurt.nelson@eversource.com

Attn: Lauren Cote-Municipal Outreach

Phone: 603-634-2409

Email: lauren.cote@eversource.com

Attn: Sam Eames-Construction Rep

Phone: 603-915-0073

Email: sam.eames@eversource.com

Attn: Thomas Meister-Construction Rep

Phone: 339-987-7901

Email: Thomas.meister@eversource.com

Attn: Joshua Scott-ROW Safety Mgr

Phone: 603-848-7759

Email: Joshua.scott@eversource.com

Contractors

JCR Utility Construction Co., Inc.

Attn: Matt Moreau-Project Manager

Phone: 603-895-4062

Email: matt.moreau@crutility.com

McCourt Construction

Attn: Michael Worhunsky-Project Manager

Phone: 617-293-3864

Email: mworhunsky@mccourtconstruction.com

Attn: Scott Gorman-Safety Director

Phone: 617-828-8822

Email: sgorman@mccourtconstruction.com

Attn: Dan Cedrone-Superintendent

Phone: 617-908-2660

Email: dcedrone@mccourtconstruction.com

Supreme Industries

Attn: Jamieson Boucher

Phone: 860-485-4101

Email: dcedrone@mccourtconstruction.com

GZA

Attn: Lucas Turcotte

Phone: 603-380-5017

Email: lucas.turcotte@gza.com

Environmental Consultant

Normandeau Associates, Inc.

Attn: Matt Smith-Environmental Monitor

Phone: 228-224-0098

Email: msmith@normandeau.com

Attn: Brian Emlaw – Environmental Monitor

Phone: 315-250-2525

Email: bemlaw@normandeau.com

Attn: Marc Jacobs-CPESC, NHCWS

Phone: 603-534-7645

Email: jaconbs2wetsoil2004@yahoo.com

Attn: Sarah Allen-Principal Wetland
Scientist

Phone: 603-714-3085

Email: sallen@normandeau.com
