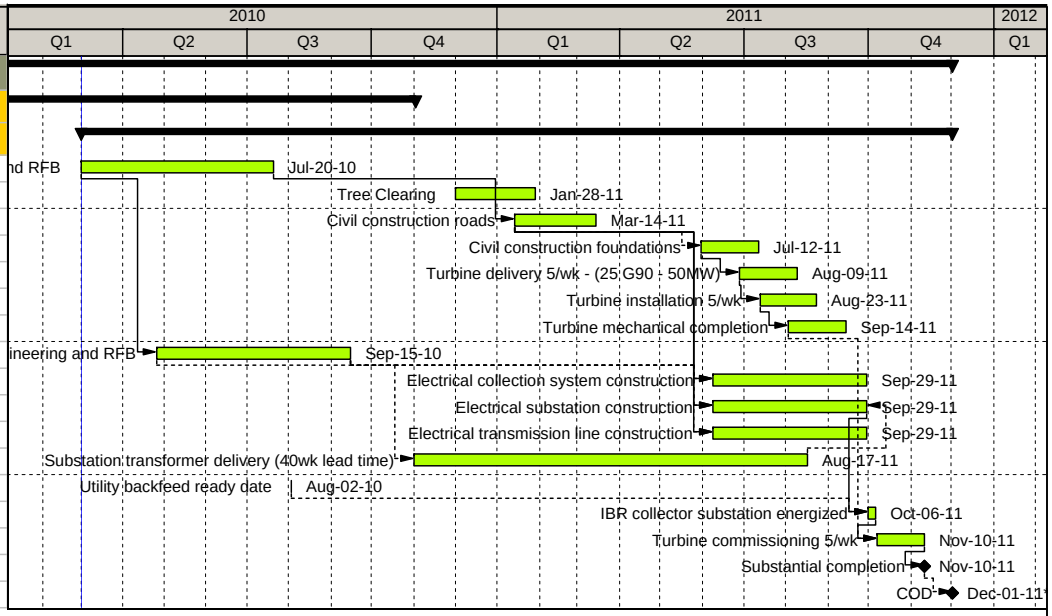Activity Name	Activity ID	Start	Finish
Groton Development Schedule		Nov-01-04 A	Dec-01-11
Groton Development		Nov-01-04 A	Nov-01-10
Groton Construction		Mar-01-10	Dec-01-11
Civil engineering and RFB	MIL-2000	Mar-01-10*	Jul-20-10
Tree Clearing	MIL-2010	Dec-01-10*	Jan-28-11
Civil construction roads	MIL-2020	Jan-14-11*	Mar-14-11
Civil construction foundations	MIL-2030	May-31-11*	Jul-12-11
Turbine delivery 5/wk - (25 G90 - 50MW)	MIL-2040	Jun-28-11*	Aug-09-11
Turbine installation 5/wk	MIL-2050	Jul-13-11	Aug-23-11
Turbine mechanical completion	MIL-2060	Aug-03-11	Sep-14-11
Electrical engineering and RFB	MIL-2075	Apr-26-10*	Sep-15-10
Electrical collection system construction	MIL-2080	Jun-08-11	Sep-29-11
Electrical substation construction	MIL-2090	Jun-08-11	Sep-29-11
Electrical transmission line construction	MIL-2100	Jun-08-11	Sep-29-11
Substation transformer delivery (40wk lead time)	MIL-2105	Nov-01-10*	Aug-17-11
Utility backfeed ready date	MIL-2107	Aug-02-10*	Aug-02-10
IBR collector substation energized	MIL-2110	Sep-30-11	Oct-06-11
Turbine commissioning 5/wk	MIL-2115	Oct-07-11	Nov-10-11
Substantial completion	MIL-369		Nov-10-11
COD	MIL-370		Dec-01-11*
